

Wood / Coal Burning Stove / Mobile Home Tie Down Supplemental Application

Applicant: _____

Location #: _____

Wood / Coal Burning Stove Report

Type of Stove: _____

Type of Fuel: _____

Stove installed by: Owner
 Licensed Contractor

Condition of Stove: Good
 Fair
 Poor

What type of floor protection: _____

What type of wall protection: _____

Is there at least 1" inch air space between the stove wall and protective shield and wall? Yes No

Type of Chimney: _____

Date Chimney was last cleaned: _____

Condition of Chimney: Good
 Fair
 Poor

Do all masonry chimneys have approved professionally installed inserts? Yes No

Stove Pipe Yes No Number of elbows: _____


Do any pass through walls and/or ceilings? Yes No

If yes, is a ventilated thimble being used? Yes No

Is a heat saver being used? Yes No

Stove Clearances

1. Side of unit to nearest wall: _____
2. Rear of unit to wall: _____
3. Top of stove pipe to ceiling: _____
4. Bottom of unit to floor: _____
5. Front of unit to front edge of floor protection: _____

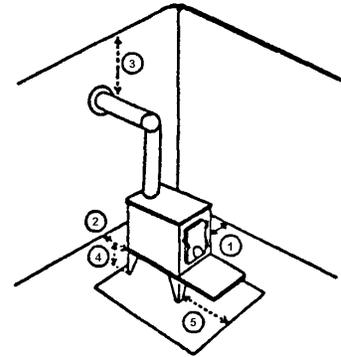

Mobile Home Tie Down Report

Make of mobile home: _____

Model: _____ Length: _____

Year built: _____ Year installed: _____

Minimum Tie Down Requirements

Length of Home	Frame Ties and Anchors per Side	Over Home Ties
Up to 40'	4	2
41' to 60'	6	3
61' to 82'	8	4

Does the Mobile Home meet the above minimum tie down requirements? Yes No

How deep are the anchors? _____ (Feet)
